

OISSION


The Virginia Railway Express, a joint project of the Northern Virginia Transportation Commission and the Potomac Rappahannock Transportation Commission, will provide safe, cost-effective, accessible, reliable, convenient, and customer responsive commuter-oriented rail passenger service. VRE contributes to the economic vitality of its member jurisdictions as an integral part of a balanced, intermodal regional transportation system.



CEO REPORT I JANUARY 2020


TABLE OF CONTENTS

3
4
6
7
8
<u>9</u>
10
11
12
13
15









PARKING UTILIZATION

The total number of parking spaces used in the VRE system during the month, divided by the total number of parking spaces available.

AVERAGE DAILY RIDERSHIP

The average number of boardings each operating day inclusive of Amtrak Step-Up boardings but excluding "S" schedule operating days.

Same month, previous year: 17,552

ON-TIME PERFORMANCE

Percentage of trains that arrive at their destination within five minutes of the schedule.

Same month, previous year: 86%



SYSTEM CAPACITY

The percent of peak hour train seats occupied. The calculation excludes reverse flow and non-peak hour trains.



OPERATING RATIO

The monthly operating revenues divided by the monthly operating expenses, which depicts the percent of operating costs paid by the riders.


Board-established goal: 52%

ON-TIME PERFORMANCE

OUR RECORD

	November 2019	October 2019	November 2018
Manassas Line	75%	77%	82%
Fredericksburg Line	83%	81%	91%
System Wide	79%	79%	86%

PRIMARY REASON FOR DELAY

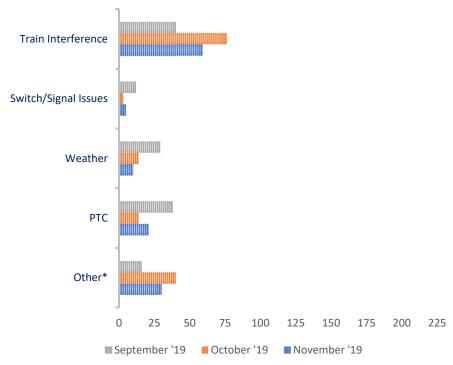

^{*}Includes trains that were delayed due to operational testing and passenger handling.

VRE operated 588 trains in November. Our ontime rate for November was 79 percent.

One hundred twenty-five trains arrived more than five minutes late to their final destinations. Of those late trains, 74 were on the Manassas Line (59 percent), and 51 were on the Fredericksburg Line (41 percent).


At 79 percent, systemwide on-time performance remained steady. There were no major shifts in delay numbers by category. Slight reductions in one area were offset by slight increases in others.

LATE TRAINS


	System Wide			Fredericksburg Line			Manassas Line			
	Sept.	Oct.	Nov.	Sept.	Oct.	Nov.	Sept.	Oct.	Nov.	
Total late trains	135	147	125	62	66	51	73	81	74	
Average minutes late	14	14	15	15	15	12	14	14	17	
Number over 30 minutes	7	9	6	5	7	I	2	2	5	
Heat restrictions	7	3	0	7	3	0				


ON-TIME PERFORMANCE

VRE SYSTEM

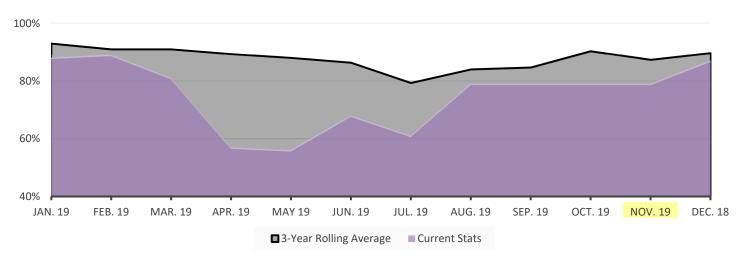


FREDERICKSBURG LINE

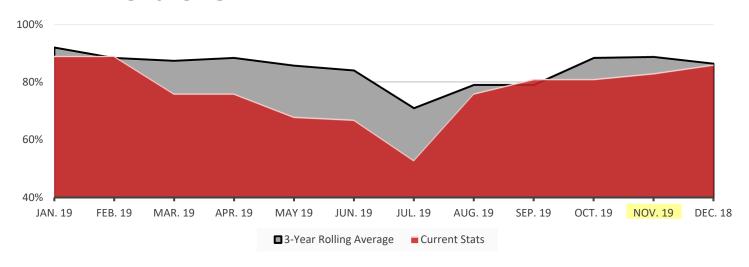

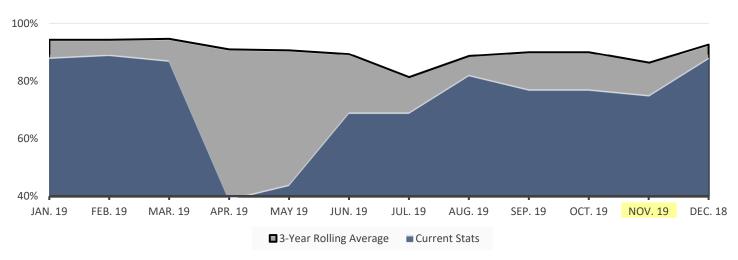



AVERAGE DAILY RIDERSHIP

VRE SYSTEM

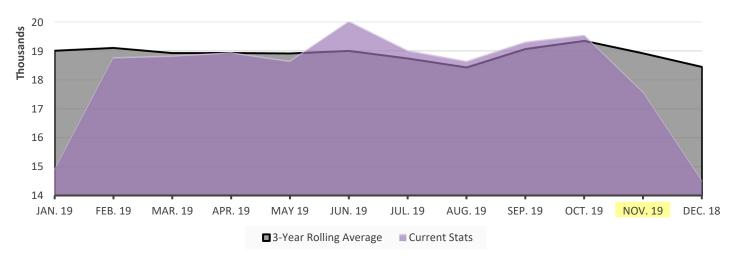

FREDERICKSBURG LINE

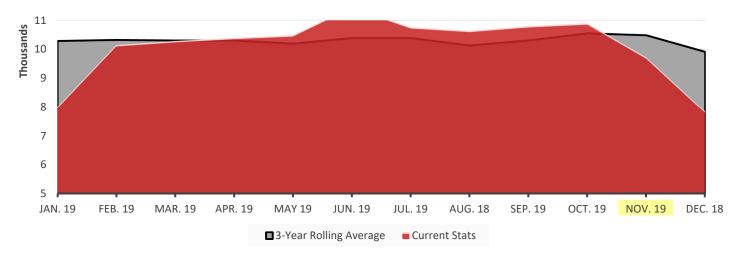

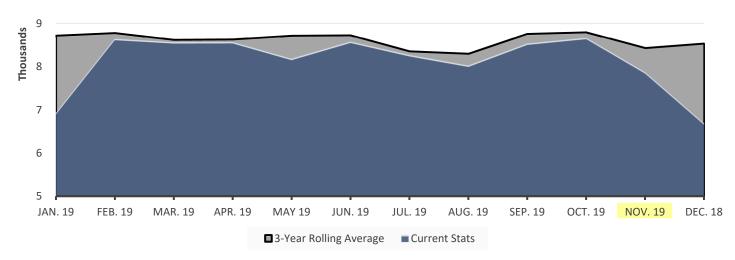


RIDERSHIP UPDATES

Average daily ridership (ADR) in November was approximately 17,600.

	November 2019	October 2019	November 2018
Monthly Ridership	334,031	430,142	351,049
Average Daily Ridership	17,581	19,552	17,552
Full Service Days	19	22	20
"S" Service Days	I	0	I

SUMMONSES ISSUED


VRE SYSTEM



SUMMONSES WAIVED OUTSIDE OF COURT


Reason for Dismissal **Occurrences** Passenger showed proof of a 20 monthly ticket 13 One-time courtesy 6 Per the request of the conductor 0 Defective ticket 0 Per ops manager 0 Unique circumstances Insufficient information 0 Lost and found ticket 0 4 Other Total Waived 43


MONTHLY SUMMONSES COURT ACTION

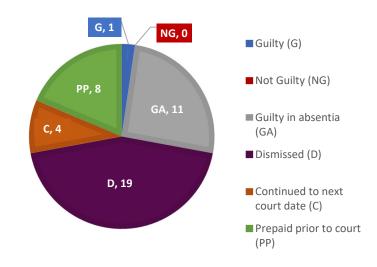

TRAIN UTILIZATION


FREDERICKSBURG LINE

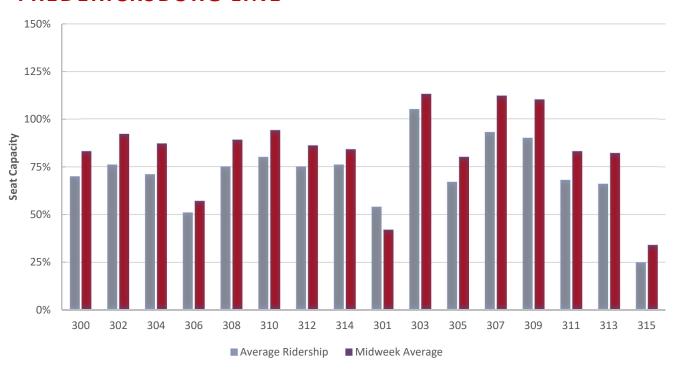


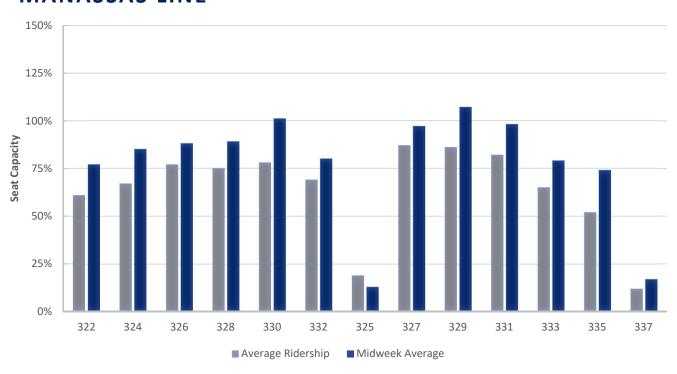

PARKING UTILIZATION

FREDERICKSBURG LINE

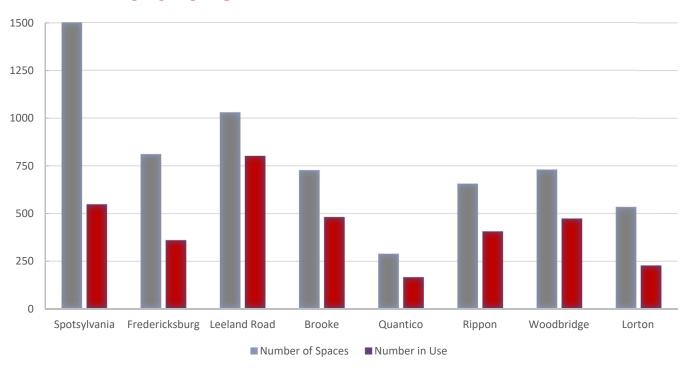

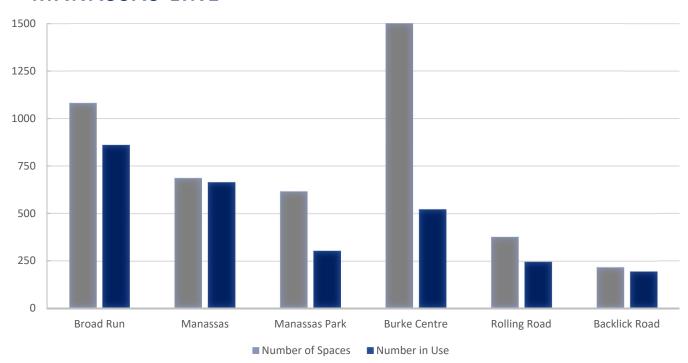

FINANCIAL REPORT

Fare revenue through the first five months of FY 2020 is approximately \$217,000 above budget (a favorable variance of 1.2 percent) and is 4.1 percent above the same period in fiscal year 2019.

The operating ratio through November is 55 percent, which is above VRE's budgeted operating ratio of 53 percent for the full 12 months of fiscal year 2020. VRE is required to budget a minimum operating ratio of 50 percent.

A summary of the FY 2020 financial results through November follows, including information on major revenue and expense categories. Please note that these figures are preliminary and unaudited.

FY 2020 Operating Budget Report											
Month Ended November 30, 2019											
	CURR. MO. ACTUAL	CURR. MO. BUDGET	YTD ACTUAL	YTD BUDGET	YTD \$ VARIANCE	YTD % VARIANCE	TOTAL FY19 BUDGET				
Operating Revenue											
Passenger Ticket Revenue	3,463,128	3,303,135	18,470,965	18,254,167	216,798	1.2%	43,810,000				
Other Operating Revenue	650	16,964	116,759	93,750	23,009	24.5%	225,000				
Subtotal Operating Revenue	3,463,778	3,320,099	18,587,723	18,347,917	239,807	1.3%	44,035,000				
Jurisdictional Subsidy (1)	-	-	9,062,029	9,062,209	(180)	0.0%	13,230,397				
Federal/State/Other Jurisdictional Subsidy	2,594,357	2,575,792	13,404,956	13,199,401	205,555	1.6%	31,462,978				
Appropriation from Reserve/Other Income	-	-	-	-	-	0.0%	-				
Interest Income	106,203	37,698	666,180	208,333	457,847	219.8%	500,000				
Total Operating Revenue	6,164,338	5,933,590	41,720,889	40,817,860	903,029	2.2%	89,228,375				
Operating Expenses											
Departmental Operating Expenses	5,364,883	5,928,690	33,631,454	36,235,690	2,604,236	7.2%	82,991,618				
Debt Service	518,480	518,480	2,592,429	2,592,399	(30)	0.0%	6,221,757				
Other Non-Departmental Expenses	3,472	1,131	18,500	6,250	(12,250)	0.0%	15,000				
Total Operating Expenses	5,886,835	6,448,301	36,242,383	38,834,338	2,591,955	6.7%	89,228,375				
Net income (loss) from Operations	277,504	(514,711)	5,478,506	1,983,521	3,494,985		-				
						Budgeted	53%				
Operating Ratio			55%	51%		Goal	50%				

⁽¹⁾ Total jurisdictional subsidy is \$17,767,748. Portion shown as budgeted is attributed to Operating Fund only.

FACILITIES UPDATE

The following is a status update of VRE facilities projects.

Completed projects:

- I. Removal of abandoned vehicle from Rippon Station through coordination with Prince William County Police
- 2. Installation of electrical conduits and conductors for Variable Messaging System (VMS) at Fredericksburg Station

Exterior of abandoned car at Rippon

Projects scheduled to be completed this quarter:

- 1. Installation of electrical conduits and conductors for Variable Messaging System (VMS) at Alexandria Station
- 2. Development of IFB for modernization of east elevator at Woodbridge Station



Interior of abandoned car at Rippon

- 3. Development of IFB for canopy roof replacement at Backlick Road Station
- 4. Development of IFB for painting of Franconia-Springfield Station
- 5. Development of IFB for pavement repairs and restriping at Rippon and Leeland Road Stations and Fredericksburg VRE Lot E

Projects scheduled to be initiated this quarter:

- I. Issuance of GEC Task Order for design of platform widening at L'Enfant Station
- 2. Issuance of GEC Task Order for design of minor structural repairs at Franconia-Springfield, Woodbridge, Rippon and Brooke Stations
- 3. Issuance of GEC Task Order for design of Phase 2 renovations to Alexandria Headquarters Suite
- 4. Development of IFB or RFQ for emergency generator overhaul project at Alexandria Headquarters, Woodbridge Station, Manassas Station and Fredericksburg VRE office

Ongoing projects:

- 1. Replacement of parking lot entrance signs at various stations
- 2. Replacement of waste and recycling receptacles at various stations
- 3. Design of Phase 2 renovations to Alexandria Headquarters Suite 202

UPCOMING PROCUREMENTS

- Construction of the Lifecycle Overhaul and Upgrade Facility
- Program management services
- Canopy roof replacement at the Backlick Road Station
- Modernization of VRE Woodbridge Station east elevator
- Passenger car wheelchair lift assemblies
- Construction of Rolling Road Station platform extension
- Purchase of LED light fixtures
- Construction of L'Enfant south storage track wayside power
- Variable Messaging System replacement
- Tactile strip replacements
- Pavement repairs and striping at the Rippon and Leeland Road stations and Fredericksburg Lot G
- Franconia-Springfield Station painting services
- Website management services
- Purchase of forklift trucks
- Final design services for VRE Broad Run expansion
- · Safety and security consulting services
- · Renewal of locomotive head end power engine systems
- Construction of Quantico Station improvements
- Construction management services for the Quantico Station Improvements project
- Mechanical engineering consulting services

CAPITAL PROJECTS UPDATES

The following is a status update of VRE capital projects.

Completed projects or major project milestones:

- 1. Long Bridge Project Environmental Impact Statement (study by others) Draft environmental impact statement, which identifies a preferred alternative and examines its impacts, was released and published in the Federal Register; DDOT and FRA are reviewing public comments to be addressed in the final environmental impact statement expected in the Summer of 2020.
- 2. New York Avenue Midday Storage Replacement Facility continuing due-diligence activities on potential property acquisitions; preliminary design effort has been completed and continue collaboration with Amtrak on project agreements.

Projects or project phases scheduled to be completed this quarter:

- 3. Franconia-Springfield Station Improvements (FRS) Draft 90% design plans
- 4. Lorton Station Second Platform (LOR) Draft 90% design plans
- 5. Rippon Station Improvements (RIP) Final 30% design plans
- 6. Brooke Station Improvements (BKV) Final 30% design plans
- 7. Leeland Road Station Improvements (LLR) Final 30% design plans
- 8. Broad Run Expansion (BRX) Section 106 Consultation
- 9. Construction of Benchmark Road Slope Stabilization (Hamilton to Crossroads closeout)

Projects or project phases scheduled to be initiated this quarter:

- 10. IFB for construction of Rolling Road Station Improvements
- 11. Request for proposals (RFP) advertised for LOU Construction Management

Ongoing projects:

- 12. Broad Run Expansion (BRX)
- 13. Manassas Park Parking Improvements
- 14. Rolling Road Station Improvements
- 15. Crossroads Maintenance and Storage Facility (MSF) land acquisition completed
- 16. Lifecycle Overhaul & Upgrade Facility (LOU)
- 17. Benchmark Road Slope Stabilization (Hamilton to Crossroads closeout)
- 18. Leeland Road Station Improvements
- 19. Brooke Station Improvements
- 20. Quantico Station Improvements
- 21. Rippon Station Improvements
- 22. Lorton Station Second Platform
- 23. Franconia-Springfield Station Improvements
- 24. Alexandria Station Improvements
- 25. Alexandria Station Track I Access (Slaters Lane)
- 26. Crystal City Station Improvements
- 27. L'Enfant Train Storage Track South
- 28. L'Enfant Station Improvements
- 29. New York Avenue Midday Storage Facility
- 30. Potomac Shores VRE Station design by others
- 31. Washington Union Station Improvements Environmental Impact Statement study by others
- 32. DC2RVA Environmental Impact Statement study by others

Projects Progress Report Follows

PASSENGER

PROJECT	DESCRIPTION	CD	PD	EC	RW	FD	CN
Alexandria Station Improvements	Eliminate at-grade track crossing, add elevators, modify platforms.	•	•	•	N/A	•	
	Modify Slaters Lane Interlocking for passenger trains on Track #1.	•	•	•	N/A	•	
	Extend and widen East Platform and elevate West Platform.	•	•	•	N/A	•	
Franconia-Springfield Station Improvements	Extend both platforms and widen East Platform for future third track.	•	•	*	N/A	•	
Lorton Station Improvements	Construct new second platform with pedestrian overpass. À	•	•	•	N/A	•	
Rippon Station Improvements	Extend existing platform, construct new second platform with pedestrian overpass. À	•	•	•	N/A		
Potomac Shores Station Improvements	New VRE station and parking in Prince William County provided by private developer.	•	•	•	N/A		
Quantico Station Improvements	Extend existing platform, construct new second platform with pedestrian overpass.	•	•	•	N/A	•	
Brooke Station Improvements	Extend existing platform, construct new second platform with pedestrian overpass. À	•	•	•	N/A		
Leeland Road Station Improvements	Extend existing platform, construct new second platform with pedestrian overpass. À	•	•	•	N/A		
Manassas Park Parking Improvements	Parking garage to increase parking capacity to 1,100 spaces.	•	•	•	N/A		
Rolling Road Station Improvements	Extend existing platform and rehabilitate existing station	•	•	•	N/A	•	•
Crystal City Station Improvements	Replace existing side platform with new, longer island platform.	•	•	•	N/A		
L'Enfant Station Improvements	Replace existing platform with wider, longer island platform. Add fourth track (VA-LE)	•			N/A		

PHASE: CD - Conceptual Design PE - Preliminary Engineering EC - Environment Clearance RW - Right of Way Acquisition FD - Final Design CN - Construction STATUS: ◆ Completed ■ Underway ■ On Hold ● part of the "Penta-Platform" program

¹ Total project cost estimate in adopted FY2020 CIP Budget; percentage complete based on VRE Operations Board authorization

² Does not include minor (< \$50,000) operating expenditures

^{*} \$2,181,630 authorization divided across five "Penta-Platform" program stations

ESTIMATED COSTS (\$)	STATUS

	ES	TIMATED COSTS	(\$)					STATUS
Total ¹	Funded	Unfunded	Authorized	Expended ²	Percent Complete ¹	Project Completion Date		
31,875,014	31,875,014	-	2,382,759	2,193,257	90%	4th QTR 2020		Design underway. Stakeholder meetings held 3/I and 4/3.
7,000,000	7,000,000	-	467,500	270,487	60%	2nd QTR 2019		Materials continue to be delivered. Assembly of cross-over has begun.
2,400,000	400,000	2,000,000	-	-	5%	4th QTR 2020		Design work on east platform only; west platform improvements unfunded.
13,000,000	13,000,000	-	*	539,149	30%	4th QTR 2022		FD underway with anticipated completion 4th QTR 2019.
16,150,000	16,150,000	-	*	756,530	30%	4th QTR 2022		FD underway with anticipated completion 4th QTR 2019.
16,634,793	16,634,793	-	*	387,599	20%	4th QTR 2023	•	PE design/EC anticipated completion 4th QTR 2019.
ı	No costs for VRE.	Private develope	r providing station	n.	10%	TBD	•	Potomac Shores VRE Station design underway to include parking structure.
18,372,949	18,372,949	0	388,784	830,833	30%	TBD		FD start 1st QTR 2019. SMART SCALE grant agreement pending.
23,391,019	23,391,019	-	*	374,663	20%	4th QTR 2023		DRPT LONP received; REF grant pending. PE design/EC anticipated completion 4th QTR 2019.
15,527,090	15,527,090	-	*	342,169	20%	4th QTR 2023		DRPT LONP received; REF grant pending. PE design/EC anticipated completion 4th QTR 2019.
25,983,000	25,983,000	0	2,238,144	670,225	30%	4th QTR 2022		Meeting held with Governing Body on 4/3. FD continues.
2,000,000	2,000,000	-	640,503	418,887	70%	3rd QTR 2020		Invitation for Bids (IFB) pending NS Construction Agreement and Fairfax County Building Permit.
49,940,000	19,098,463	30,841,537	1,584,619	397,848	30%	2nd QTR 2024	•	PE & EC initiated in Oct 2019 and anticipated completion 3rd QTR 2020.
70,650,000	62,465,721	8,184,279	130,501	65,150	50%	2nd QTR 2023	•	DRPT LONP received. Real estate research in progress under LONP.

TRACK AND INFRASTR			PH	IASE			
PROJECT	DESCRIPTION	CD	PD	EC	RW	FD	CN
Hamilton-to-Crossroads Third Track	2½-miles of new third track with CSXT design and construction of signal and track tie-ins.	•	•	•	N/A	•	•
MAINTENANCE AND S	TORAGE FACILITIES						
L'Enfant Train Storage Track - South	Enfant Train Storage Track - South Conversion of CSXT Temporary Track to VRE Storage Track (1,350 feet) and Associated Signal Work					•	•
Lifecycle Overhaul & Upgrade Facility	New LOU facility to be added to the Crossroads MSF.	•	•	•	N/A	•	•
Crossroads Maintenance and Storage Facility - Land Acquisition	Acquisition of 19.5 acres of land, construction of two storage tracks and related site improvements.	•	N/A	N/A	•	N/A	N/A
New York Avenue Midday Storage Replacement Facility	Midday storage facility replacement for Ivy City storage facility.	•	•	•	•		
ROLLING STOCK							
Passenger Railcar Procurement	Acquisition of 29 new railcars.	•	N/A	N/A	N/A	•	•
Positive Train Control	Implement Positive Train Control for all VRE locomotives and control cars.	•	N/A	N/A	N/A	•	•
PLANNING, COMMUNI Broad Run Expansion	CATIONS AND IT NEPA and PE for expanding						
(was Gainesville-Haymarket Extension)	commuter rail service capacity in Western Prince William County	•	•	•	-	-	-
Mobile Ticketing	Implementation of a new mobile ticketing system.	•	N/A	N/A	N/A	•	•
PHASE: CD - Conceptual Design Plof Way Acquisition FD - Final Design STATUS: • Completed • Underv	E - Preliminary Engineering EC - Enviror CN - Construction vay On Hold	ıment	: Clear	ance		RW -	Right

¹ Total project cost estimate in adopted FY2020 CIP Budget; percentage complete based on VRE Operations Board authorization

² Does not include minor (< \$50,000) operating expenditures

	EST	IMATED COSTS	(\$)					STATUS
Total ¹	Funded	Unfunded	Authorized	Expended ²	Percent Complete ¹	Project Completion Date		
32,500,000	32,500,000	-	33,285,519	30,578,003	90%	3rd QTR 2018	♦	Close-out pending repair of storm damage to embankment.
3,965,000	3,965,000	-	2,937,323	1,699,610	60%	4th QTR 2019		CSXT Construction Agreement received. CM underway.
38,183,632	38,183,632	-	3,176,039	2,143,583	70%	TBD		Completion of FD pending completion of land acquisition.
2,950,000	2,950,000	-	2,950,000	163,565	100%	Ist QTR 2020		Land acquistion has been completed.
89,666,508	89,666,508	-	3,588,305	2,087,050	75%	4th QTR 2021		Preliminary design has been completed and continuing to collaborate with Amtrak on agreements.
75,264,693	75,264,693	-	69,457,809	47,915,644	99%	4th QTR 2020	♦	All cars received. Completion date reflects end of warranty period.
14,191,833	14,191,833	-	10,294,079	7,984,451	95%	4th QTR 2018		Implementation Completed. Final stabilization and familiarization phase in process.
110,700,000	82,526,398	28,173,602	5,855,650	4,539,446	80%	4th QTR 2024		PE design and EC underway. Property acquisition due diligency underway.
3,510,307	3,510,307	-	3,510,627	2,282,853	70%	3rd QTR 2019		Big Commerce/Moovel collaboration undeway for web based ticketing portal. Uplift to new platform scheduled for mid-summer.

